

State of Texas

§

County of Galveston

§

§

AGREEMENT FOR ENGINEERING SERVICES

PARTIES

This Agreement for Engineering Services (the “Agreement”) is made and entered into by and between the County of Galveston, a political subdivision of the State of Texas, acting by and through its Galveston County Commissioners Court (the “County”), and **Tetra Tech, Inc.** (the “Engineer”), each of whom is a Party hereto and who are collectively referred to herein as the Parties.

RECITALS

The County conducted a Request for Qualifications, Number RFQ 25-079, entitled “Professional Services for Future Engineering Projects” (the “RFQ”), to procure professional engineering services to perform the engineering services for the **Dickinson Bayou Desnagging** project within the County (the “Project”), which is further described herein and which such services are within the scope of the practice of engineering.

The Engineer timely submitted a statement of qualifications in the RFQ, is a licensed engineer in the State of Texas, and wishes to perform said services.

Now Therefore, for and in consideration of the covenants and agreements contained herein, the receipt and sufficiency of which is hereby acknowledged, the Parties agree as follows:

CONTRACTUAL UNDERTAKINGS

SECTION I RETENTION OF ENGINEER

The County, by and through this Agreement, retains the Engineer to perform professional engineering services in connection with the Project, and the Engineer, by and through this Agreement, agrees to perform said professional engineering services in connection with the Project.

This Agreement means this document (pages 1 through 9), the RFQ, which includes but is not limited to any addenda thereto, if any, the Engineer’s response in the RFQ (i.e., its’ statement of qualifications, certifications, affidavits, and vendor information), and all Exhibits affixed hereto, if any, all of which are incorporated herein for all purposes. Exhibits to be physically affixed, if any, shall be affixed following the signature/execution page of this Agreement. The RFQ, all addenda therein, if any, and Engineer’s response therein shall be retained in the Galveston County Purchasing Agent’s Office.

**SECTION II
CHARACTER AND EXTENT OF SERVICES**

The Engineer shall render professional engineering services necessary for the development of the Project, limited to the following and performed in accordance with existing local, State and Federal regulations, as set out in the Scope of Services attached hereto as Exhibit "A".

The Scope of Services and Response attached hereto as Exhibit "A" is also made a part of this Agreement for all purposes. But, if any terms of Exhibit "A" conflicts with any existing State of Texas, Texas Department of Transportation, local, or Federal laws, rules or regulations, the State, Federal or local laws, rules or regulations shall control.

The character and extent of services outlined above shall be considered complete upon approval by County, acting by and through its County Engineer, of the various drawings, data and tasks outlined in Exhibit "A".

All Services provided by Engineer shall be of good quality and shall be performed in a professional manner. The standard of care for all professional engineering and related Services performed or furnished by Engineer and the Response under this Agreement will be the care and skill ordinarily used by other competent engineers practicing under the same or similar circumstances and professional license. Engineer will re-perform any Services not meeting this standard without additional compensation. Engineer will perform its services as expeditiously as is prudent considering the ordinary professional skill and care of a competent engineer.

Additional services that may be required after approval of these documents by the County, or required by State or Federal regulations published in the State or Federal Register after the date of execution of this Agreement, shall not be considered as covered by the maximum amount payable under this Contract as provided in Section V. Compensation for such extra services shall be as provided in Section V except that the maximum amount payable shall be revised by agreement between County and Engineer.

**SECTION III
PERIOD OF SERVICES**

This Agreement shall be effective upon execution by the County and by the Engineer, with the date of the Party signing last in time, and shall remain in force until satisfactory completion of all services described herein or termination under the provisions hereinafter provided in section VIII.

After execution of Agreement, Engineer shall submit a Project Time Schedule to the County Engineer, which shall be diligently followed during performance of services. It is understood by the County that the Engineer will make every effort to expedite completion of the Project.

**SECTION IV
COORDINATION WITH THE COUNTY**

The Engineer agrees to perform the services diligently after authorization to proceed. The Engineer agrees to perform all other services diligently and within the agreed upon time schedule.

The Engineer shall hold periodic conferences with the County Engineer to the end that the Project, as perfected, shall have full benefit of the County's experience and knowledge of existing needs and facilities and be consistent with the County's current policies and construction standards. To implement this coordination, the County Engineer shall make available to the Engineer for use in the Project, all existing plans, maps, field notes, statistics, computations and other data in its possession relative to the Project. Engineer shall submit a monthly progress report of project status to the County Engineer and the County Engineer is the County's designated point of contact for this Agreement.

SECTION V THE ENGINEERS'S COMPENSATION

As set forth in Exhibit "A" attached hereto, the County shall compensate the Engineer for services performed under this Agreement per the compensation amounts shown in Exhibit "A" for design and construction phase services.

Notwithstanding the foregoing, the maximum amount payable under this Contract is **\$452,600** including expenses. The maximum amount payable may be revised in the event of changes in extent, complexity, or character of work requiring such revisions upon the prior mutual, written agreement by the County and the Engineer. No revisions in the maximum amount payable will be permitted unless previously authorized in writing by the County.

Payments to the Engineer for authorized services will be made by the County within 45 calendar days upon presentation of monthly statements by the Engineer to the County reflecting Engineer's performance of such services, unless disputed by the County. Additionally, the County agrees that it shall review the monthly statements and if disputing, shall notify the Engineer of the County's dispute no later than thirty (30) days after the County's receipt of the monthly statement. All remittances shall be mailed or delivered to Engineer's office. Engineer further agrees that all monthly statements shall detail its services under this Agreement and, if this Agreement is funded through Federal dollars, comply with applicable Federal requirements associated with costs.

SECTION VI OWNERSHIP OF DOCUMENTS

Original documents, plans, designs and survey notes ("Documents") belong to and remain the property of the County, in consideration of which it is mutually agreed that the County will use them solely in connection with the Project or as required by law, save with the express consent of the Engineer. The Engineer may retain copies of such Documents.

County contracts are subject to all legal requirements provided by county, state or federal statutes, rules and regulations.

Engineer acknowledges that Galveston County is a governmental entity which conducts its meetings in accordance with the Texas Open Meetings Act and whose certain records are available to the public under the Texas Public Information Act. In accordance with Title 5, Chapters 551 and 552 of the Texas Government Code, this Agreement is an open record under the Public Information Act and as such, will be discussed and voted upon in a public meeting. Any request made to either

inspect or acquire a copy of this Agreement or the Documents produced as a result of this Agreement will not violate the terms of this Agreement.

SECTION VII DISPUTE RESOLUTION

If a dispute arises out of or relates to a breach of this Agreement, and if the dispute cannot be settled through negotiation, then the Engineer and the County agree to submit the dispute to mediation. In the event the Engineer or the County desires to mediate any dispute, it shall notify the other Party in writing of the dispute desired to be mediated. If the Parties are unable to resolve their differences within ten days of the receipt of such notice, such dispute shall be submitted for mediation in accordance with the procedures and rules of the American Arbitration Association (or any successor organization) then in effect. The deadline for submitting the dispute to mediation can be changed if the Parties mutually agree in writing to extend the time between receipt of notice and submission of mediation. The expenses of the mediator shall be shared 50 percent by the Engineer and 50 percent by the County. This requirement to seek mediation shall be a condition required before filing an action at law or in equity.

SECTION VIII TERMINATION

The County may terminate the Agreement with or without cause, or for convenience by giving to the Engineer at least thirty (30) calendar days' advance notice in writing. Upon receipt or delivery of such notice, the Engineer shall discontinue all services in connection with the performance of this Agreement and shall proceed to cancel promptly all existing orders and contracts insofar as such orders or contracts are chargeable to this Agreement. As soon as practicable after receipt of notice of termination, the Engineer shall submit a statement showing in detail, the services performed under this Agreement to the date of termination.

The County shall then pay the Engineer promptly for that portion of the prescribed charges which the services actually performed under this Agreement bear to the total services called for under the Agreement, less such payments on account of the charges as have been previously made. Copies of all completed or partially completed surveys, reports, designs, plans, specifications and all other documents prepared under this Agreement shall be delivered to the County Engineer when and if this agreement is terminated, but subject to the restrictions, as to their use, as set forth in Section VI.

SECTION IX INSURANCE

The Engineer shall obtain and maintain, throughout the term of the Agreement, insurance of the types and in the minimum amounts set forth below.

The Engineer shall, upon request by the County, furnish certificates of insurance to the County evidencing compliance with the insurance requirements herein. Certificates shall indicate name of the Engineer, name of insurance company, policy number, and terms and limits of coverage. The Engineer shall cause its insurance companies to provide the County with at least thirty (30)

days' prior written notice of any reduction in the limit of liability by endorsement of the policy, cancellation or non-renewal of the insurance coverage required under this Agreement. The Engineer shall obtain such insurance from such companies having a Best's rating of B+/VII or better, licensed or approved to transact business in the state in which the Services shall be performed, Texas, and shall obtain such insurance of the following types and minimum limits.

a. Workers' Compensation insurance in accordance with the Laws of the State of Texas, or state of hire/location of Services, and Employer's Liability coverage with a limit of not less than \$500,000 each employee for Occupational Disease; \$500,000 policy limit for Occupational Disease; and Employer's Liability of \$500,000 each accident.

b. Commercial General Liability insurance including coverage for Products/Completed Operations, Blanket Contractual, Contractors' Protective Liability, Broad Form Property Damage, Personal Injury/Advertising Liability, and Bodily Injury and Property Damage with limits of not less than:

\$2,000,000	general aggregate limit
1,000,000	each occurrence, combined single limit
1,000,000	aggregate Products, combined single limit
1,000,000	aggregate Personal Injury/Advertising Liability
50,000	Fire Legal Liability
5,000	Premises Medical

c. Business Automobile Liability coverage applying to owned, non-owned and hired automobiles with limits not less than \$1,000,000 each occurrence combined single limit for Bodily Injury and Property Damage combined.

d. Umbrella Excess Liability insurance written as excess of Employer's Liability, with limits not less than \$1,000,000 each occurrence combined single limit.

e. Professional Liability insurance with limits not less than \$1,000,000 each claim/annual aggregate.

The County and the County's agents and employees shall be added as additional insureds to all coverages required above, except for those requirements in paragraphs "a" and "e". All policies written on behalf of the Engineer shall contain a waiver of subrogation in favor of the County and the County's agents and employees, with the exception of insurance required under paragraph "e". Additionally, the Contractor's commercial general liability insurance must provide any defense provided by the policy to Galveston County, its officials, employees, and agents.

**SECTION X
VENUE AND CHOICE OF LAW**

This Agreement shall be construed and enforced for all purposes pursuant to the laws of the State of Texas. Venue shall lie exclusively in a court of competent jurisdiction in Galveston County, Texas.

**SECTION XI
ADDRESS OF NOTICES AND COMMUNICATIONS**

All notices and communications under this Agreement to be mailed or delivered to Engineer shall be to the following address:

Name: Bart Standley
Title: Vice President
Mailing Address: 575 N. Dairy Ashford
Suite 700
Houston, Texas 77079

All notices and communications under this Agreement to be mailed or delivered to the County shall be to the following address:

Mark Henry, Galveston County Judge
Galveston County Courthouse
722 Moody, 2nd Floor
Galveston, Texas 77550

With a copy to:

Michael Shannon, PE, CFM,
Galveston County Engineer
722 Moody, 1st Floor
Galveston, Texas 77550

**SECTION XII
SECTION CAPTIONS**

Each section under the contractual undertakings has been supplied with a caption to serve only as a guide to the contents. The caption does not control the meaning of any section or in any way determine its interpretation or application.

**SECTION XIII
SUCCESSORS AND ASSIGNS**

The County and the Engineer each binds itself and its successors, and assigns to the other Party of this Agreement and to the successors, and assigns of such other Party in respect to all provisions of this Agreement. Except as above, neither the County nor the Engineer shall assign, subcontract, or otherwise transfer their interest in this Agreement without the prior written consent of the other Party. Nothing herein shall be construed as creating any personal liability on the part of any officer or agent of any public body which may be a party thereto.

**SECTION XIV
ADDITIONAL TERMS**

14.1 PROCUREMENT REQUIREMENTS

Engineer shall comply with all applicable local, State, and Federal laws, rules, regulations, orders, and ordinances. This includes, but is not limited to, that Engineer shall comply with the Galveston County Purchasing Policies & Procedures Manual approved by Order of the Commissioners Court on March 7, 2018, including without limitation, applicable provisions within Chapter Nine of said Manual as this contract is made pursuant to a federal award.

14.2 CONFLICT OF INTEREST

a. No member of the County's governing body, and no employee, officer, or agent of the County shall participate in the selection or in the award of administration of a subcontract supported by grant funds if a conflict of interest, real or apparent, would be involved. Such a conflict of interest would arise when: 1.) the employee, officer, or agent, 2.) any member of his or her immediate family, 3.) his or her partner, or 4.) any organization which employs, or is about to employ any of the above; has a financial or other interest in the firm or person selected to perform the subcontract.

b. In all cases not governed by Subsection (a) of this Section, no person specified in subsection (c) of this Section, who exercises any functions or responsibilities in connection with the planning and carrying out of the project, or who are in a position to participate in decision making process or gain inside information with regard to activities under this Agreement as Amended, may obtain a financial interest or benefit from the activity, or have an interest or benefit from the activity, or have any interest in any contract, subcontract, or agreement with respect thereto, or the proceeds thereunder, either for themselves or those with whom they have family or business ties during their tenure or for (1) year thereafter.

c. The conflict of interest provisions of Subsection (b) apply to any person who is an employee, agent, consultant, officer, elected official, or appointed official of the County or of the Contractor.

14.3 AUTHORITY TO BIND

Each Party represents and warrants for itself that the individual executing this Agreement on its behalf has the full power and authority to do so and to legally bind the Party to all the terms and provisions of this Agreement and that this Agreement constitutes the legal, valid, and binding agreement of each Party hereto.

14.4 IMMUNITY RETAINED

The County does not waive or relinquish any immunity or defense on behalf of itself, its trustees, officers, employees, and agents as a result of its execution of this Agreement and performance of the covenants contained herein. The County specifically reserves any claim it may

have to sovereign, qualified, or official immunity as a defense to any action arising in conjunction with this Agreement.

14.5 NO THIRD-PARTY BENEFICIARY

This Agreement inures only to the benefit of Galveston County and Contractor. This Agreement does not create, is not intended to create, and shall not be deemed or construed to create any rights or benefits in third parties.

14.6 SEVERABILITY

If a provision contained in this Agreement is held invalid for any reason by a court of competent jurisdiction, the invalidity shall not affect other provisions of the Agreement that may be given effect without the invalid provision, and to this end the provisions of this Agreement are severable.

14.7 VALIDITY/ENFORCABILITY

If any current or future legal limitations affect the validity or enforceability of a provision of this Agreement, then the legal limitations are made a part of this Agreement and shall operate to amend this Agreement to the minimum extent necessary to bring this Agreement into conformity with the requirements of the limitation, and as so modified, this Agreement shall continue in full force and effect.

Execution Page follows this Page

The Rest of this Page is Intentionally Left Blank

This Agreement is hereby EXECUTED by the Parties hereto in triplicate (three (3)) counterparts, each of which shall constitute an original, to be effective upon full execution with the date of the Party signing last in time.

Galveston County


Tetra Tech, Inc.

By 
Mark Henry
County Judge

By 
Bart Standley
Vice President

Date Signed: March 2, 2026

Date Signed: 1/30/2026

Attest: _____
SDwight D. Sullivan,
Galveston County Clerk
By:  Deputy
Melissa A. Childs




EXHIBIT A



January 29, 2026

Mr. Michael Shannon, PE, CFM
Galveston County
722 Moody Ave., 1st Floor
Galveston, Texas 77550

Re: Proposal for Engineering Services for Dickinson Bayou Desnagging
Located in Galveston County, Texas

Dear Mr. Shannon,

Tetra Tech appreciates the opportunity to provide Galveston County (Client) with this proposal for professional engineering services to prepare plans, contact documents, bid phase and construction phase services for the desnagging and clearing of nearly 21 miles of Dickinson Bayou and associated tributaries in Galveston County. These limits are detailed in Exhibit A.

A schedule for the completion of the construction documents and project construction for the stream improvements is also provided as Exhibit B. The fee estimate is based on the following information.

PROJECT UNDERSTANDING

Tetra Tech understands the engineering services to include preparation of plans, specifications, engineer's probable construction cost, environmental assessment, limited survey, bid phase services and construction phase services for de-s snagging and selectively clearing a cumulative 21 miles of Dickinson Bayou and associated tributaries as depicted in Exhibit A.

Maps shown in Exhibit A include those from the City of Dickinson Natural Resources Conservation Service (NRCS) grant funded desnagging project as well a map from the 2025 Galveston County Bond election for desnagging of Dickinson Bayou. This proposal considers the cumulative total of both of these projects and eliminates any overlap.

SCOPE OF BASIC PROFESSIONAL ENGINEERING SERVICES

Basic Services

Task I – Project Management & Coordination (6 months for Design Phase)

- I. Attend kick-off meeting consisting of the Program Manager, the County, and the City to confirm and coordinate the requirements of the project.

2. Supervise and coordinate various items of work within the project design, including review of activities of subcontracted engineers.
3. Provide coordination and information to help the City of Dickinson grant requirements and general coordination with the City of Dickinson.
4. Provide monthly status reports (6).
5. Meet up to 4 times with the County (online or at the Galveston County Engineering office) to discuss project status and review comments.

Task 2 – Engineering Design

1. 60% Preliminary Design & Agency Coordination
 - a. Begin general data collection including aerials and LiDAR.
 - b. Coordinate USACE backup documentation and project notification.
 - c. Coordinate for Texas Historical Commission backup documentation and project notification.
 - d. Perform drone reconnaissance and field visit.
 - i. Verify buildings, docks, structures, aerial power lines and pipelines that we will need to be avoided and verify survey
 - ii. Identify areas where debris tends to build up from conversations with officials, local residents and from reconnaissance visits.
 - iii. Review all available aerial images, videos, survey, LiDAR and other supporting data.
 - iv. Identify trees that are close to the waterway and that are leaning in towards the waterway at 30 degrees or more that might be more likely to fall into the water.
 - v. Identify logs or stumps that are located within the waterway that may impact the flow of water or that may be causing the collection of debris.
 - vi. Identify trees and areas where the overhanging branches are close to the top of water (within top of water to less than 5 feet above the water that may cause the collection of debris during storm events.
 - vii. Identify areas where the undergrowth might be too thick and therefore might be contributing to the development of debris dams during storm events.
 - viii. Identify special trees to avoid/protect.
 - ix. Identify hazardous debris.
 - e. Begin coordination for private utility map requests and develop utility matrix.
 - f. Review available hydrologic and hydraulic models (as applicable) to understand the watershed.
 - b. Identify potential debris storage/mulching sites.
 - c. Prepare 60% Plan Set (56 sheets estimated) including:
 - i. Cover, General Notes & Legend (4 sheets)
 - ii. Survey Control Sheets (10)
 - iii. Overall Project Layout (1"=600') (8)
 - iv. Desnagging Plan Sheets (1"=100') (27)
 - v. Details/Typicals (5)
 - vi. Offsite Mulch Sites (1)
 - vii. Haul Routes/Access Plan (1)
 - d. Prepare a 60% cost estimate.
 - e. Perform QAQC on plans and cost estimate.
 - f. Submit 60% plans and cost estimate to the County for review.
2. 95% Design
 - a. Address 60% plan comments from the County & City.
 - b. Begin coordination with TxDOT for any permits.

- c. Continue private utility coordination.
 - d. Develop a Waste Management Plan.
 - e. Prepare 95% Plan Set (57 sheets estimated) including:
 - a. Cover, General Notes & Legend (4 sheets)
 - b. Survey Control Sheets (10)
 - c. Overall Project Layout (1"=600') (8)
 - d. Desnagging Plan Sheets (1"=100') (27)
 - e. Details/Typicals (5) – Including traffic control
 - f. Offsite Mulch Sites (1)
 - g. Haul Routes/Access Plan (1)
 - h. Client Project Sign (1)
 - f. Prepare a 95% cost estimate.
 - g. Prepare technical specifications.
 - h. Perform QAQC on plans, specifications, and cost estimate.
 - i. Submit 95% plans and cost estimate to the County for review.
3. 100% Design
- a. Address 95% plan comments from the County.
 - b. Obtain permits as required from the Texas Department of Transportation.
 - c. Finalize the Waste Management Plan.
 - d. Prepare 100% Plan Set including Cover, General Notes & Legend, Overall Plan, Desnagging Plan Sheets, Desnagging Details, Traffic Control Details, Offsite Mulch Sites, Haul Routes, and Client Project Sign.
 - e. Prepare a 100% cost estimate.
 - f. Prepare final technical specifications.
 - g. Perform QAQC on plans, specifications, and cost estimate.
 - h. Submit 100% plans and cost estimate to the County for acceptance.

Task 3 – Bid Phase Services

- 1. Prepare Notice to bidders for use by County in advertising the project.
- 2. Provide one hard copy of bid documents to local bid service.
- 3. Answer questions of bidders and suppliers during bidding.
- 4. Assist county in conducting pre-bid conference.
- 5. Issue addenda as required.
- 6. Attend bid opening.
- 7. Check bids for errors and responsiveness and tabulate results.
- 8. Assist County in reviewing qualifications of apparent low bidder.
- 9. Issue a recommendation for award.

Task 4 – Construction Management/Observation

- 1. Assist County with pre-construction meeting including preparing an agenda and meeting minutes.
- 2. Document, log and address submittals from the contractor.
- 3. Document, log, and address requests for information from the contractor.
- 4. Assist the County in reviewing any change orders.
- 5. Receive and review progress pay estimates for the contractor.
- 6. Provide on-site project observation during construction phase. Site visits (200 maximum assumed) will be conducted on a daily basis to check the progress and quality of the executed work of the Construction Contractor and to determine, in general, if such work is in accordance with the Construction Contract.
- 7. Assist County in coordinating with residents.

8. Perform substantial completion inspection with the County.
9. Provide substantial completion checklist and certificate of substantial completion.
10. Perform final inspection with the contractor and the County to determine completeness of the Project.
11. Prepare record drawings to conform to construction records, as-built construction plans, data, or other information provided by the Contractor and the County as needed.

Tetra Tech Expenses

1. Mileage for Site Visits
2. Map Request Fees

Additional Services – Survey (as needed, to be provided by owner)

1. Provide a recoverable baseline with TBM’s on-site. TBM’s shall be tied to the Texas State Plane Coordinate System, South Central Zone (NAD 83) and NAVD 88.
2. Prepare and submit Survey Control Maps, in an acceptable format, signed and sealed by a Registered Professional Land Surveyor.
3. Galveston County Appraisal District mapping info will be downloaded and populated as a GIS background map for land data. Owner name and parcel ID will be included. No Deed or Easement Research will be performed and no Boundary Survey related tasks will be performed in the field or office.
4. Final submittal shall consist of an AutoCAD file, Signed and Sealed Survey Control PDF’s (24”x36”), and CSV point file).

FEES

The fees for each phase of the project are outlined below and will be billed on a Lump Sum Basis.

BASIC SERVICES

<u>Task</u>	<u>Fee Basis</u>	<u>Fee Amount</u>
Task 1 – Project Management & Coordination	Lump Sum	\$ 37,100
Task 2 – Engineering Design		
60% Preliminary Design & Agency Coordination	Lump Sum	\$ 137,400
95% Design	Lump Sum	\$ 58,700
100% Design	Lump Sum	\$ 28,900
Task 3 - Bid Phase Services	Lump Sum	\$ 11,500
Task 4 - Construction Management/Observation	Lump Sum	\$ 163,000
 Tetra Tech Expenses (Estimated)	 T&M	 \$ <u>16,000</u>
 Total		 \$ 452,600

This proposal is based on the following assumptions:

- No detailed survey will be performed for this project. Galveston County parcel data and LiDAR will be used to develop drawings. If needed, spot survey can be provided as mentioned in the Additional Services by the Client.

Mr. Michael Shannon, PE, CFM
Proposal for Engineering Services for Dickinson Bayou Desnagging
January 29, 2026

- County will provide right of entry coordination for environmental/survey work. Secure any needed rights of entry/temporary construction easements. County will confirm that field teams have 100% survey access to conduct the proposed survey prior to field mobilization.
- No official public meetings will be held, only some resident coordination.
- No site-specific job training will be required for field personnel.
- A USACE verification request/meeting is not included for the wetland delineation. No Section 404 permitting is included as part of this scope of services.
- The preparation of a mitigation plan and calculation of potential mitigation costs (for wetlands) is not included.
- Wetland and stream functional assessments are not included.
- No cultural field work is included.
- No direct NRCS uploads will take place for plan submittals or invoicing.
- No geotechnical services will be necessary for this scope of work.
- LiDAR will be the primary source of elevation information.
- All files will be delivered in electronic format unless stated otherwise.
- No cross-section sheets will be required.
- Construction Phase Services assume that no more than 200 days will be needed for site visits.

These services, if required, and upon agreement from the Client, will be performed as an additional service.

We appreciate the opportunity to submit this proposal to you and look forward to working with you on this important project. If you have any questions or need additional information, please do not hesitate to call Bart Standley, P.E. or me at your convenience.

Sincerely,



Natalie Chaney, P.E., ENV SP
Tx Stormwater & Sustainability Lead

Attachments: Exhibit A & B

EXHIBIT A


EWP Site Location Map

Date: 10/31/2024

Client(s): City of Dickinson

Assisted By: Asa Logan
USDA-NRCS
ANGLETON SERVICE CENTER
BRAZORIA COUNTY SOIL & WATER CONSERVATION DISTRICT

Approximate Acres:

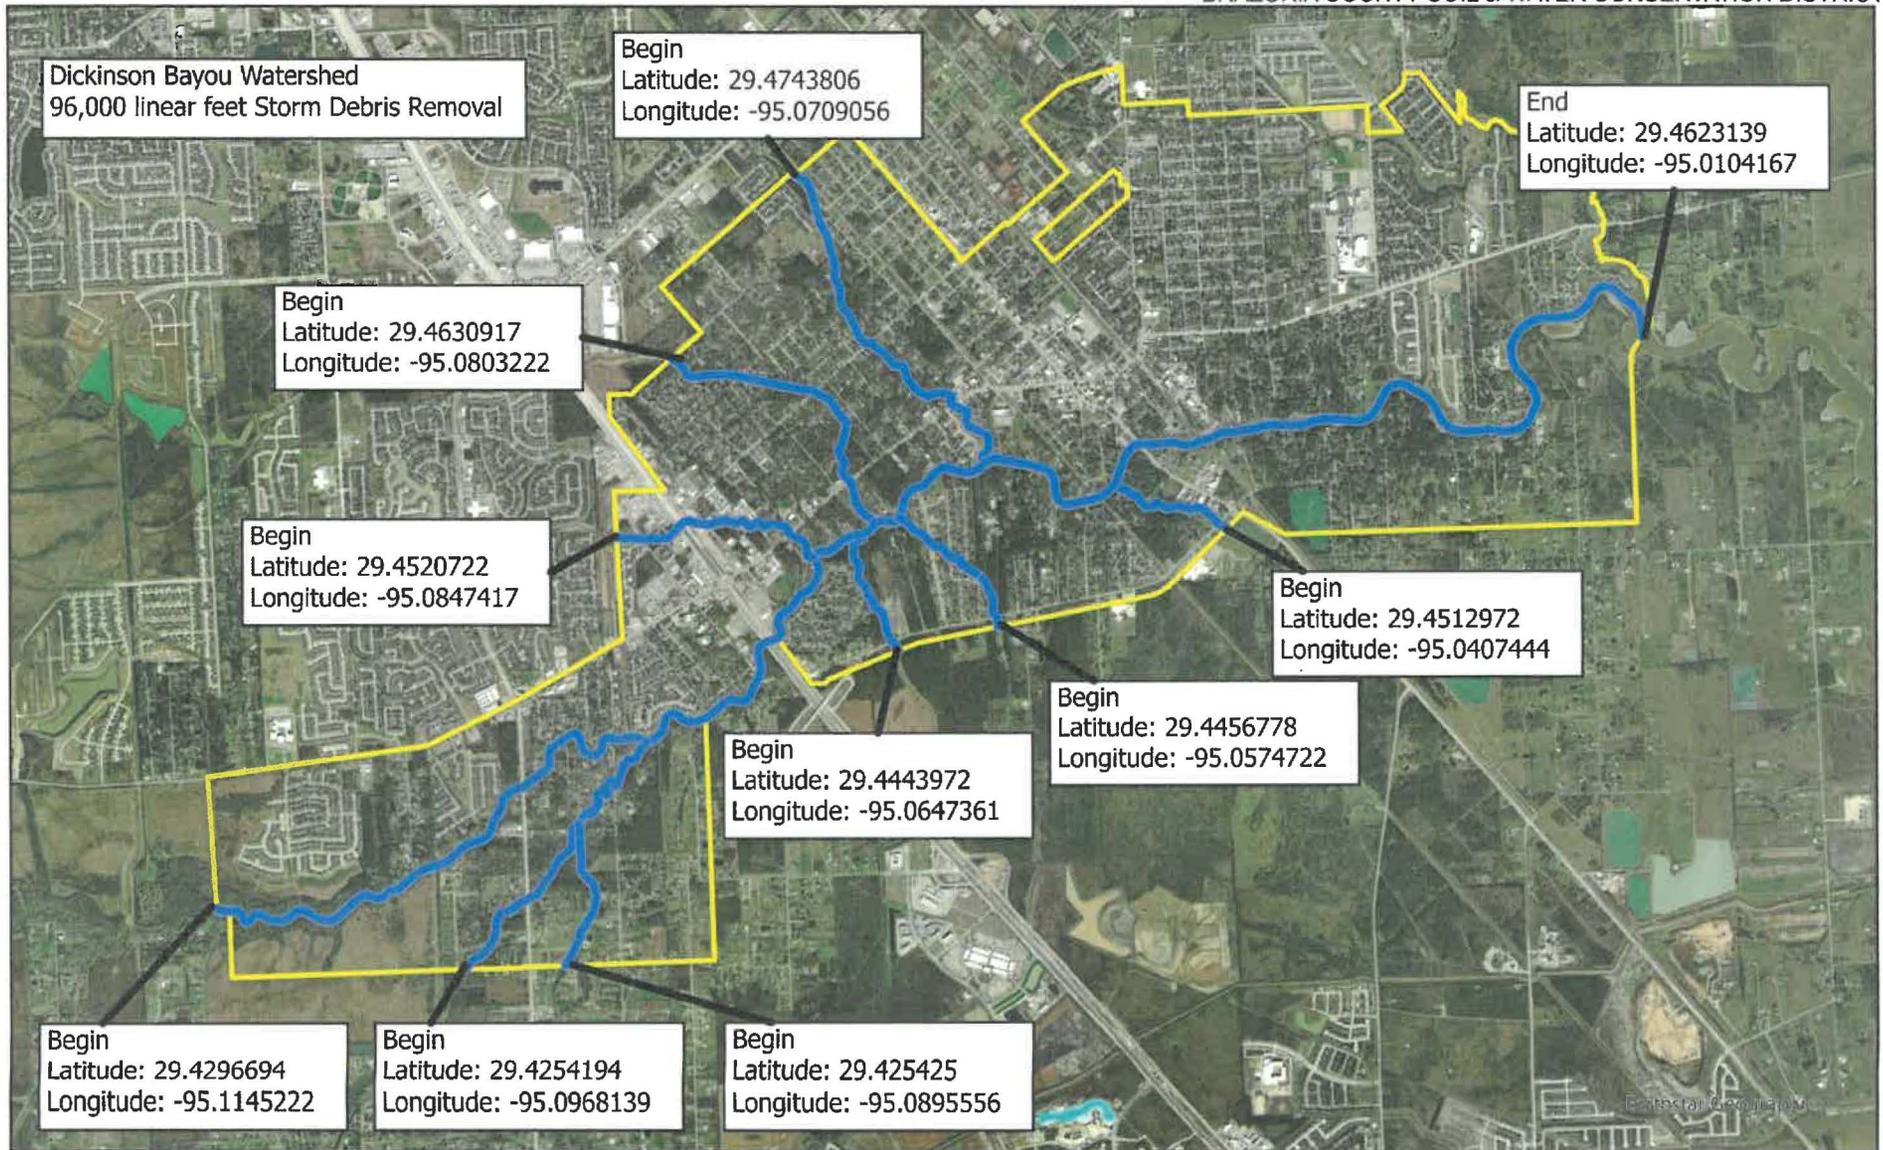

Streams
City



Prepared with assistance from USDA-Natural Resources Conservation Service

USDA is an equal opportunity provider, employer, and lender

EXHIBIT A

LEAGUE CITY

Bay Colony

58850 ft

FM 517 Rd W

FM 517 Rd W

FM 517 Rd W

DICKINSON

TEXAS CITY

Crescent Ranch Estates

SANTA FE

FM 1884 Rd



VICINITY MAP
1:1,706,667


PROJECT NAME: DICKINSON BAYOU
 CITY: LEAGUE CITY, DICKINSON, AND SANTA FE
 PRECINCT: 2
 FACILITY: DRAINAGE DISTRICT #1
 FACILITY: BAYOU
 DESCRIPTION: CLEARING AND DESNAGGING
 ENGINEER'S ESTIMATE: \$1,680,000
 PROJECT CONSTRAINTS:
 1. ENVIRONMENTAL PERMITTING

Legend

- Dickinson_Bayou_Watershed
- Dickinson Bayou



1:40,000
Date: 12/10/2024



GALVESTON COUNTY
2025 MOBILITY BOND PROGRAM



